PHILIPPINE BIDDING DOCUMENTS

(As Harmonized with Development Partners)



Procurement of INFRASTRUCTURE PROJECTS Concrete overlay along C.S. Umali Street at C.S. Umali Street Barangay Quinale

Government of the Republic of the Philippines

Sixth Edition July 2020

Preface

These Philippine Bidding Documents (PBDs) for the procurement of Infrastructure Projects (hereinafter referred to also as the "Works") through Competitive Bidding have been prepared by the Government of the Philippines for use by all branches, agencies, departments, bureaus, offices, or instrumentalities of the government, including government-owned and/or -controlled corporations, government financial institutions, state universities and colleges, local government units, and autonomous regional government. The procedures and practices presented in this document have been developed through broad experience, and are for mandatory use in projects that are financed in whole or in part by the Government of the Philippines or any foreign government/foreign or international financing institution in accordance with the provisions of the 2016 revised Implementing Rules and Regulations (IRR) of Republic Act (RA) No. 9184.

The PBDs are intended as a model for admeasurements (unit prices or unit rates in a bill of quantities) types of contract, which are the most common in Works contracting.

The Bidding Documents shall clearly and adequately define, among others: (i) the objectives, scope, and expected outputs and/or results of the proposed contract; (ii) the eligibility requirements of Bidders; (iii) the expected contract duration; and (iv) the obligations, duties, and/or functions of the winning Bidder.

Care should be taken to check the relevance of the provisions of the PBDs against the requirements of the specific Works to be procured. If duplication of a subject is inevitable in other sections of the document prepared by the Procuring Entity, care must be exercised to avoid contradictions between clauses dealing with the same matter.

Moreover, each section is prepared with notes intended only as information for the Procuring Entity or the person drafting the Bidding Documents. They shall not be included in the final documents. The following general directions should be observed when using the documents:

- a. All the documents listed in the Table of Contents are normally required for the procurement of Infrastructure Projects. However, they should be adapted as necessary to the circumstances of the particular Project.
- b. Specific details, such as the "name of the Procuring Entity" and "address for bid submission," should be furnished in the Instructions to Bidders, Bid Data Sheet, and Special Conditions of Contract. The final documents should contain neither blank spaces nor options.
- c. This Preface and the footnotes or notes in italics included in the Invitation to Bid, BDS, General Conditions of Contract, Special Conditions of Contract, Specifications, Drawings, and Bill of Quantities are not part of the text of the final document, although they contain instructions that the Procuring Entity should strictly follow.
- d. The cover should be modified as required to identify the Bidding Documents as to the names of the Project, Contract, and Procuring Entity, in addition to date of issue.

- e. Modifications for specific Procurement Project details should be provided in the Special Conditions of Contract as amendments to the Conditions of Contract. For easy completion, whenever reference has to be made to specific clauses in the Bid Data Sheet or Special Conditions of Contract, these terms shall be printed in bold typeface on Sections I (Instructions to Bidders) and III (General Conditions of Contract), respectively.
- f. For guidelines on the use of Bidding Forms and the procurement of Foreign-Assisted Projects, these will be covered by a separate issuance of the Government Procurement Policy Board.

TABLE OF CONTENTS

Glos	ssar	y of Terms, Abbreviations, and Acronyms	5
Sect	ion	I. Invitation to Bid	8
Sect	ion	II. Instructions to Bidders	12
1	1.	Scope of Bid	15
2	2.	Funding Information	15
3	3.	Bidding Requirements	15
۷	1 .	Corrupt, Fraudulent, Collusive, Coercive, and Obstructive Practices	15
4	5.	Eligible Bidders	
ϵ	5.	Origin of Associated Goods	16
7	7.	Subcontracts	16
8	3.	Pre-Bid Conference	17
ç	€.	Clarification and Amendment of Bidding Documents	17
1	10.	Documents Comprising the Bid: Eligibility and Technical Components	17
1	11.	Documents Comprising the Bid: Financial Component	18
1	12.	Alternative Bids	18
1	13.	Bid Prices	18
1	14.	Bid and Payment Currencies	18
1	15.	Bid Security	19
1	16.	Sealing and Marking of Bids	19
1	17.	Deadline for Submission of Bids	19
1	18.	Opening and Preliminary Examination of Bids	19
1	19.	Detailed Evaluation and Comparison of Bids	19
2	20.	Post Qualification	20
2	21.	Signing of the Contract	20
Sect	ion	III. Bid Data Sheet	21
Sect	ion	IV. General Conditions of Contract	24
1	1.	Scope of Contract	25
2	2.	Sectional Completion of Works	25
3	3.	Possession of Site	
۷	1.	The Contractor's Obligations	25
5	5.	Performance Security	
ϵ	5.	Site Investigation Reports	26

7.	Warranty	26
8.	Liability of the Contractor	26
9.	Termination for Other Causes	26
10.	Dayworks	27
11.	Program of Work	27
12.	Instructions, Inspections and Audits	27
13.	Advance Payment	27
14.	Progress Payments	27
15.	Operating and Maintenance Manuals	27
Section	V. Special Conditions of Contract	29
Section	VI. Specifications	31
Section	VII. Drawings	39
	VIII. Bill of Quantities	
	IX. Checklist of Technical and Financial Documents	

Glossary of Terms, Abbreviations, and Acronyms

ABC – Approved Budget for the Contract.

ARCC – Allowable Range of Contract Cost.

BAC – Bids and Awards Committee.

Bid – A signed offer or proposal to undertake a contract submitted by a bidder in response to and in consonance with the requirements of the bidding documents. Also referred to as *Proposal* and *Tender*. (2016 revised IRR, Section 5[c])

Bidder – Refers to a contractor, manufacturer, supplier, distributor and/or consultant who submits a bid in response to the requirements of the Bidding Documents. (2016 revised IRR, Section 5[d])

Bidding Documents – The documents issued by the Procuring Entity as the bases for bids, furnishing all information necessary for a prospective bidder to prepare a bid for the Goods, Infrastructure Projects, and/or Consulting Services required by the Procuring Entity. (2016 revised IRR, Section 5[e])

BIR – Bureau of Internal Revenue.

BSP – Bangko Sentral ng Pilipinas.

CDA – Cooperative Development Authority.

Consulting Services – Refer to services for Infrastructure Projects and other types of projects or activities of the GOP requiring adequate external technical and professional expertise that are beyond the capability and/or capacity of the GOP to undertake such as, but not limited to: (i) advisory and review services; (ii) pre-investment or feasibility studies; (iii) design; (iv) construction supervision; (v) management and related services; and (vi) other technical services or special studies. (2016 revised IRR, Section 5[i])

Contract – Refers to the agreement entered into between the Procuring Entity and the Supplier or Manufacturer or Distributor or Service Provider for procurement of Goods and Services; Contractor for Procurement of Infrastructure Projects; or Consultant or Consulting Firm for Procurement of Consulting Services; as the case may be, as recorded in the Contract Form signed by the parties, including all attachments and appendices thereto and all documents incorporated by reference therein.

Contractor – is a natural or juridical entity whose proposal was accepted by the Procuring Entity and to whom the Contract to execute the Work was awarded. Contractor as used in these Bidding Documents may likewise refer to a supplier, distributor, manufacturer, or consultant.

CPI – Consumer Price Index.

DOLE – Department of Labor and Employment.

DTI – Department of Trade and Industry.

Foreign-funded Procurement or Foreign-Assisted Project – Refers to procurement whose funding source is from a foreign government, foreign or international financing institution as specified in the Treaty or International or Executive Agreement. (2016 revised IRR, Section 5[b]).

GFI – Government Financial Institution.

GOCC – Government-owned and/or –controlled corporation.

Goods — Refer to all items, supplies, materials and general support services, except Consulting Services and Infrastructure Projects, which may be needed in the transaction of public businesses or in the pursuit of any government undertaking, project or activity, whether in the nature of equipment, furniture, stationery, materials for construction, or personal property of any kind, including non-personal or contractual services such as the repair and maintenance of equipment and furniture, as well as trucking, hauling, janitorial, security, and related or analogous services, as well as procurement of materials and supplies provided by the Procuring Entity for such services. The term "related" or "analogous services" shall include, but is not limited to, lease or purchase of office space, media advertisements, health maintenance services, and other services essential to the operation of the Procuring Entity. (2016 revised IRR, Section 5[r])

GOP – Government of the Philippines.

Infrastructure Projects – Include the construction, improvement, rehabilitation, demolition, repair, restoration or maintenance of roads and bridges, railways, airports, seaports, communication facilities, civil works components of information technology projects, irrigation, flood control and drainage, water supply, sanitation, sewerage and solid waste management systems, shore protection, energy/power and electrification facilities, national buildings, school buildings, hospital buildings, and other related construction projects of the government. Also referred to as *civil works or works*. (2016 revised IRR, Section 5[u])

LGUs – Local Government Units.

NFCC – Net Financial Contracting Capacity.

NGA – National Government Agency.

PCAB – Philippine Contractors Accreditation Board.

PhilGEPS - Philippine Government Electronic Procurement System.

Procurement Project – refers to a specific or identified procurement covering goods, infrastructure project or consulting services. A Procurement Project shall be described, detailed, and scheduled in the Project Procurement Management Plan prepared by the agency which shall be consolidated in the procuring entity's Annual Procurement Plan. (GPPB Circular No. 06-2019 dated 17 July 2019)

PSA – Philippine Statistics Authority.

SEC – Securities and Exchange Commission.

 ${\bf SLCC-Single\ Largest\ Completed\ Contract}.$

UN – United Nations.

Section I. Invitation to Bid



Republic of the Philippines Province of Laguna Municipality of Paete

Tel. Nos. (049) 501-6490-101, (049) 557-0001

Invitation to Bid Improvement of Concrete overlay along C.S. Umali Street at C.S. Umali Street Barangay Quinale

1. The *Municipality of Paete, Laguna*, through the 20% *Development Fund* intends to apply the sum of *five hundred twenty thousand eight hundred sixteen pesos and 72/100 only (Php 520,816.72)* being the Approved Budget for the Contract (ABC) to payments under the contract for *Concrete Overlay along C.S. Umali Street at C.S. Umali Street Barangay Quinale, Paete, Laguna* Bids received in excess of the ABC shall be automatically rejected at bid opening.

Description of Work

	8 9		COTTNE Pr	nilinnine			HG LAC
	8 _db 8	Republic of the Philippines Province of Laguna				(3)	W WWW E
			MUNICIPALITY OF PAETE			City.	
	The Cale					10	A SO LONG
	INDIV	'IDUAL I	PROGRA	AM O	FWORKS		-
NAME/L	OCATION OF PROJECT			Net A	\rea	m3	50.25
CO	NCRETE OVERLAY AONG C.S. UN	ΛΔΙΙ STE	PEET	Tota	Length	m	134 m.
	MONETE OVEREAT AONO 0.0. UI	IIALI OTT	\	Width		m	2.50 m
CSI	JMALI STREET, BARANGAY -4, QU	IINAI F I	PAFTF				
0.0.	LAGUNA.	,, .	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	Thick	nes	m	0.15 m.
				CALE	ENDAR DAYS TO C	OMPLETE	60 days
PROJEC	CT CATEGORY :			DES	IRABLE STARTING	DATE	
PROJEC	CT DESCRIPTION						
	OONODETE OV	/EDL AX A	01000		LOTDEET		
	CONCRETE OV	/ERLAY A	ONG C.S	. UIVIAL	ISIREEI		
	MINIMUM EQUIPMENT REQUIREMENT			TE	CHNICAL PERSON	INEL REQU	IIRED
	Description	N	lo.	D	escription		No.
					Foreman		1
	CONCRETE MIXER	1			Mason / Carper	iter	3
					Laborer		6
					We Dir		
	ESTIMATED I		PROP	T		IRECT CO	et .
Item No.	DESCRIPTION	%OF TOTAL	UNIT	QTY.	TOTAL	IKECT CO	UNIT COST
1	MOBILIZATION / DEMOBILIZATION		l.s.	1			
	TEMPORARY FACILITIES		l.s.	1			
III	CONCRETING		l.s.	1			
IV.	RSB		l.s.	1			
V	FORMWORKS		l.s.	1			
VI.	PROJECT SIGNAGE		l.s.	1			
\ /11	SAFETY & HEALTH		l.s.	1			
VII.							

- 2. The *Municipality of Paete*, *Laguna* now invites bids for the above Procurement Project. Completion of the Works is required *60 calendar days*. Bidders should have completed a contract similar to the Project. The description of an eligible bidder is contained in the Bidding Documents, particularly, in Section II (Instructions to Bidders).
- 3. Bidding will be conducted through open competitive bidding procedures using non-discretionary "pass/fail" criterion as specified in the 2016 revised Implementing Rules and Regulations (IRR) of Republic Act (RA) No. 9184.
- 4. Interested bidders may obtain further information from *Municipality of Paete*, *Laguna* and inspect the Bidding Documents at the address given below from 8:00 am to 5:00 pm Monday to Friday.
- 5. A complete set of Bidding Documents may be acquired by interested bidders on *March 26-April 13*, 2021 from given address and website/s upon payment of a nonrefundable fee for the Bidding Documents in the amount of **one thousand pesos only (Php 1000.00)**. It may also be downloaded free of charge from the website of the Philippine Government Electronic Procurement System (PhilGEPS) and the website of the Procuring Entity, provided that bidders shall pay the applicable fee for the Bidding Documents not later than the submission of their bids. The Procuring Entity shall allow the bidder to present its proof of payment for the fees *presented in person through BAC Secretariat*.
- 6. Bids must be duly received by the BAC Secretariat through manual submission at the office address as indicated below on or before *April 13*, 2021@ 9:00 am. Late bids shall not be accepted.
- 7. All bids must be accompanied by a bid security in any of the acceptable forms and in the amount stated in **ITB** Clause 16.
- 8. Bid opening shall be on *April 13*, 2021@10:30 am at the given address below *Municipal Building*, *Municipal Hall*, *J.V. Quesada St. Brgy 1*, *Paete*, *Laguna* Bids will be opened in the presence of the bidders' representatives who choose to attend the activity.

The schedule of BAC activities is as follows:

BAC Activities	Schedule
1. Advertisement/Issuance of Bidding Documents	March 26-April 13, 2021
2.Deadline of Submission of Bids	April 13, 2021 @9:00 am
3. Opening of Bids	April 13, 2021 @10:30 am

4. Bid Evaluation	April 14, 2021
5. Post-qualification	April 15-16, 2021
6. Notice of Award	April 20, 2021
7. Contract Agreement	April 30, 2021
8. Notice to Proceed	May 3, 2021

- 9. The *Municipality Of Paete*, *Laguna* reserves the right to reject any and all bids, declare a failure of bidding, or not award the contract at any time prior to contract award in accordance with Sections 35.6 and 41 of the 2016 revised Implementing Rules and Regulations (IRR) of RA No. 9184, without thereby incurring any liability to the affected bidder or bidders.
- 10. For further information, please refer to:

Christine M. Cainto
Bac Secretariat
J.V. Quesada St. B-1 Paete, Laguna
odacrem_12@yahoo.com
049-501-6490-101
Paete.gov.ph

11. You may visit the following websites:

For downloading www.Paete.gov.ph	of	Bidding	Documents:	www.philgeps.gov.ph	and
[February 5, 2021]					
			ANTONIO C		

Section II. Instructions to Bidders

INSTRUCTIONS TO BIDDERS

1. Introduction

The Municipality of Paete, Laguna, through the 20% Development Fund. intends to apply the sum of five hundred twenty thousand eight hundred sixteen pesos and 72/100 only (Php 520,816.72) being the Approved Budget for the Contract (ABC) to payments under the contract for Concrete Overlay along C.S. Umali Street at C.S. Umali Street Barangay Quinale Paete, Laguna The bidding process assumes the following timetable:

BAC Activities	Schedule
1. Advertisement/Issuance of Bidding Documents	March 26-April 13, 2021
2.Deadline of Submission of Bids	April 13, 2021 @9:00 am
3. Opening of Bids	April 13, 2021 @10:30 am
4. Bid Evaluation	April 14, 2021
5. Post-qualification	April 15-16, 2021
6. Notice of Award	April 20, 2021

The eligibility and technical documents of the Bid as specified in Section IX. Checklist of Technical and Financial Documents.

- 1. Please read Bid Data Sheet for additional requirements.
- 2. Please read Special Condition of Contract.

Note: deadline of Submission is on April 13, 2021 @9:00 am based on the Municipal Bundy clock, Late bids will not be accepted.

ANTONIO C. DELA ROSA

BAC Chairman

1. Scope of Bid

The Procuring Entity, *Municipality of Paete*, *Laguna* invites Bids for the Rehabilitation of Multi-purposed Building at J.P. Rizal St. Barangay Bagumbayan Paete, Laguna with Project Identification Number *IP-007-21-ROAD*.

[Note: The Project Identification Number is assigned by the Procuring Entity based on its own coding scheme and is not the same as the PhilGEPS reference number, which is generated after the posting of the bid opportunity on the PhilGEPS website.]

The Procurement Project (referred to herein as "Project") is for the construction of Works, as described in Section VI (Specifications).

2. Funding Information

- 2.1. The GOP through the source of funding as indicated below for **year 2021** in the amount of **FIVE HUNDRED TWENTY THOUSAND EIGHT HUNDRED SIXTEEN PESOS AND 72/100 ONLY (Php 520,816.72)**.
- 2.2. The source of funding is:
 - a. LGUs, the Annual or Supplemental Budget, as approved by the Sanggunian.

3. Bidding Requirements

The Bidding for the Project shall be governed by all the provisions of RA No. 9184 and its 2016 revised IRR, including its Generic Procurement Manual and associated policies, rules and regulations as the primary source thereof, while the herein clauses shall serve as the secondary source thereof.

Any amendments made to the IRR and other GPPB issuances shall be applicable only to the ongoing posting, advertisement, or invitation to bid by the BAC through the issuance of a supplemental or bid bulletin.

The Bidder, by the act of submitting its Bid, shall be deemed to have inspected the site, determined the general characteristics of the contracted Works and the conditions for this Project, such as the location and the nature of the work; (b) climatic conditions; (c) transportation facilities; (c) nature and condition of the terrain, geological conditions at the site communication facilities, requirements, location and availability of construction aggregates and other materials, labor, water, electric power and access roads; and (d) other factors that may affect the cost, duration and execution or implementation of the contract, project, or work and examine all instructions, forms, terms, and project requirements in the Bidding Documents.

4. Corrupt, Fraudulent, Collusive, Coercive, and Obstructive Practices

The Procuring Entity, as well as the Bidders and Contractors, shall observe the highest standard of ethics during the procurement and execution of the contract. They

or through an agent shall not engage in corrupt, fraudulent, collusive, coercive, and obstructive practices defined under Annex "I" of the 2016 revised IRR of RA No. 9184 or other integrity violations in competing for the Project.

5. Eligible Bidders

- 5.1. Only Bids of Bidders found to be legally, technically, and financially capable will be evaluated.
- 5.2. The Bidder must have an experience of having completed a Single Largest Completed Contract (SLCC) that is similar to this Project, equivalent to at least fifty percent (50%) of the ABC adjusted, if necessary, by the Bidder to current prices using the PSA's CPI, except under conditions provided for in Section 23.4.2.4 of the 2016 revised IRR of RA No. 9184.

A contract is considered to be "similar" to the contract to be bid if it has the major categories of work stated in the **BDS**.

- 5.3. For Foreign-funded Procurement, the Procuring Entity and the foreign government/foreign or international financing institution may agree on another track record requirement, as specified in the Bidding Document prepared for this purpose.
- 5.4. The Bidders shall comply with the eligibility criteria under Section 23.4.2 of the 2016 IRR of RA No. 9184.

6. Origin of Associated Goods

There is no restriction on the origin of Goods other than those prohibited by a decision of the UN Security Council taken under Chapter VII of the Charter of the UN.

7. Subcontracts

7.1. The Bidder may subcontract portions of the Project to the extent allowed by the Procuring Entity as stated herein, but in no case more than fifty percent (50%) of the Project.

The Procuring Entity has prescribed that:

- a. Subcontracting is not allowed.
- 7.1. [If Procuring Entity has determined that subcontracting is allowed during the bidding, state:] The Bidder must submit together with its Bid the documentary requirements of the subcontractor(s) complying with the eligibility criterial stated in ITB Clause 5 in accordance with Section 23.4 of the 2016 revised IRR of RA No. 9184 pursuant to Section 23.1 thereof.
- 7.2. [If subcontracting is allowed during the contract implementation stage, state:] The Supplier may identify its subcontractor during the contract

implementation stage. Subcontractors identified during the bidding may be changed during the implementation of this Contract. Subcontractors must submit the documentary requirements under Section 23.1 of the 2016 revised IRR of RA No. 9184 and comply with the eligibility criteria specified in **ITB** Clause 5 to the implementing or end-user unit.

7.3. Subcontracting of any portion of the Project does not relieve the Contractor of any liability or obligation under the Contract. The Supplier will be responsible for the acts, defaults, and negligence of any subcontractor, its agents, servants, or workmen as fully as if these were the Contractor's own acts, defaults, or negligence, or those of its agents, servants, or workmen.

8. Pre-Bid Conference

The Procuring Entity will hold a pre-bid conference for this Project on the specified date and time and either at its physical address Municipal Building, Municipal Hall J.V. Quesada st. Brgy 1 Paete, Laguna and as indicated in paragraph 6 of the **IB**.

9. Clarification and Amendment of Bidding Documents

Prospective bidders may request for clarification on and/or interpretation of any part of the Bidding Documents. Such requests must be in writing and received by the Procuring Entity, either at its given address or through electronic mail indicated in the **IB**, at least ten (10) calendar days before the deadline set for the submission and receipt of Bids.

10. Documents Comprising the Bid: Eligibility and Technical Components

- 10.1. The first envelope shall contain the eligibility and technical documents of the Bid as specified in **Section IX. Checklist of Technical and Financial Documents**.
- 10.2. If the eligibility requirements or statements, the bids, and all other documents for submission to the BAC are in foreign language other than English, it must be accompanied by a translation in English, which shall be authenticated by the appropriate Philippine foreign service establishment, post, or the equivalent office having jurisdiction over the foreign bidder's affairs in the Philippines. For Contracting Parties to the Apostille Convention, only the translated documents shall be authenticated through an apostille pursuant to GPPB Resolution No. 13-2019 dated 23 May 2019. The English translation shall govern, for purposes of interpretation of the bid.
- 10.3. A valid PCAB License is required, and in case of joint ventures, a valid special PCAB License, and registration for the type and cost of the contract for this Project. Any additional type of Contractor license or permit shall be indicated in the **BDS**.
- 10.4. A List of Contractor's key personnel (e.g., Project Manager, Project Engineers, Materials Engineers, and Foremen) assigned to the contract to be

bid, with their complete qualification and experience data shall be provided. These key personnel must meet the required minimum years of experience set in the **BDS**.

10.5. A List of Contractor's major equipment units, which are owned, leased, and/or under purchase agreements, supported by proof of ownership, certification of availability of equipment from the equipment lessor/vendor for the duration of the project, as the case may be, must meet the minimum requirements for the contract set in the **BDS**.

11. Documents Comprising the Bid: Financial Component

- 11.1. The second bid envelope shall contain the financial documents for the Bid as specified in **Section IX. Checklist of Technical and Financial Documents**.
- 11.2. Any bid exceeding the ABC indicated in paragraph 1 of the **IB** shall not be accepted.
- 11.3. For Foreign-funded procurement, a ceiling may be applied to bid prices provided the conditions are met under Section 31.2 of the 2016 revised IRR of RA No. 9184.

12. Alternative Bids

Bidders shall submit offers that comply with the requirements of the Bidding Documents, including the basic technical design as indicated in the drawings and specifications. Unless there is a value engineering clause in the **BDS**, alternative Bids shall not be accepted.

13. Bid Prices

All bid prices for the given scope of work in the Project as awarded shall be considered as fixed prices, and therefore not subject to price escalation during contract implementation, except under extraordinary circumstances as determined by the NEDA and approved by the GPPB pursuant to the revised Guidelines for Contract Price Escalation guidelines.

14. Bid and Payment Currencies

- 14.1. Bid prices may be quoted in the local currency or tradeable currency accepted by the BSP at the discretion of the Bidder. However, for purposes of bid evaluation, Bids denominated in foreign currencies shall be converted to Philippine currency based on the exchange rate as published in the BSP reference rate bulletin on the day of the bid opening.
- 14.2. Payment of the contract price shall be made in:
 - a. Philippine Pesos.

15. Bid Security

- 15.1. The Bidder shall submit a Bid Securing Declaration or any form of Bid Security in the amount indicated in the **BDS**, which shall be not less than the percentage of the ABC in accordance with the schedule in the **BDS**.
- 15.2. The Bid and bid security shall be valid until *August 11*, *2021*. Any bid not accompanied by an acceptable bid security shall be rejected by the Procuring Entity as non-responsive.

16. Sealing and Marking of Bids

Each Bidder shall submit one copy of the first and second components of its Bid.

The Procuring Entity may request additional hard copies and/or electronic copies of the Bid. However, failure of the Bidders to comply with the said request shall not be a ground for disqualification.

If the Procuring Entity allows the submission of bids through online submission to the given website or any other electronic means, the Bidder shall submit an electronic copy of its Bid, which must be digitally signed. An electronic copy that cannot be opened or is corrupted shall be considered non-responsive and, thus, automatically disqualified.

17. Deadline for Submission of Bids

The Bidders shall submit on the specified date and time and either at its physical address or through online submission as indicated in paragraph 7 of the **IB**.

18. Opening and Preliminary Examination of Bids

18.1. The BAC shall open the Bids in public at the time, on the date, and at the place specified in paragraph 9 of the **IB**. The Bidders' representatives who are present shall sign a register evidencing their attendance. In case videoconferencing, webcasting or other similar technologies will be used, attendance of participants shall likewise be recorded by the BAC Secretariat.

In case the Bids cannot be opened as scheduled due to justifiable reasons, the rescheduling requirements under Section 29 of the 2016 revised IRR of RA No. 9184 shall prevail.

18.2. The preliminary examination of Bids shall be governed by Section 30 of the 2016 revised IRR of RA No. 9184.

19. Detailed Evaluation and Comparison of Bids

19.1. The Procuring Entity's BAC shall immediately conduct a detailed evaluation of all Bids rated "passed" using non-discretionary pass/fail criteria. The BAC

shall consider the conditions in the evaluation of Bids under Section 32.2 of 2016 revised IRR of RA No. 9184.

- 19.2. If the Project allows partial bids, all Bids and combinations of Bids as indicated in the **BDS** shall be received by the same deadline and opened and evaluated simultaneously so as to determine the Bid or combination of Bids offering the lowest calculated cost to the Procuring Entity. Bid Security as required by **ITB** Clause 16 shall be submitted for each contract (lot) separately.
- 19.3. In all cases, the NFCC computation pursuant to Section 23.4.2.6 of the 2016 revised IRR of RA No. 9184 must be sufficient for the total of the ABCs for all the lots participated in by the prospective Bidder.

20. Post Qualification

Within a non-extendible period of five (5) calendar days from receipt by the Bidder of the notice from the BAC that it submitted the Lowest Calculated Bid, the Bidder shall submit its latest income and business tax returns filed and paid through the BIR Electronic Filing and Payment System (eFPS), and other appropriate licenses and permits required by law and stated in the **BDS**.

21. Signing of the Contract

The documents required in Section 37.2 of the 2016 revised IRR of RA No. 9184 shall form part of the Contract. Additional Contract documents are indicated in the **BDS**.

Section III. Bid Data Sheet

Bid Data Sheet

ITB Clause									
5.2	For this purpose, contr	acts similar to the Project	refer to contracts which have						
	the same major categories of work, which shall be:								
	Road								
7.1	Subcontracting is not a	llowed.							
10.3	Valid PCAB License								
10.4	The key personnel must meet the required minimum years of experience s below:								
	Key Personnel	General Experience	Relevant Experience						
	Project Manager,	3 years	3 years						
	Project Engineers	3 years	3 years						
	Materials Engineers	3 years	3 years						
	Foremen	3 years	3 years						
	Mason/carpenter	3 years	3 years						
	Welder	3 years	3 years						
	Part Time Practitioner								
	First Aider								
	Laborer								
10.5	The minimum major equipment requirements are the following:								
			CAL						
	Equipment Capacity Number of Units Concrete Mixer 1								
	Hands Tools		1						
12	alternative Bids shall n	ot be accepted.							
15.1	-		ecuring Declaration or any of						
	the following forms and amounts:								
			isand four hundred sixteen						
	bid security	• · • · · · · · · · · · · · · · · · · ·	[two percent (2%) of ABC], if r's/manager's check, bank						
	•	or irrevocable letter of cr							
			,						
		•	x thousand forty- pesos and						
	•		nt (5%) of ABC] if bid security						
19.2	is in Surety Box	IIU.							
20		le period of five (5) cale	ndar days from receipt by the						
20			ted the Lowest Calculated Bid,						
			business tax returns filed and						

	paid through the BIR Electronic Filing and Payment System (eFPS)
21	Additional contract documents relevant to the Project that may be required by
	existing laws and/or the Procuring Entity, such as construction schedule and S-
	curve, manpower schedule, construction methods, equipment utilization
	schedule, construction safety and health program approved by the DOLE,
	PERT/CPM and other acceptable tools of project scheduling.

Section IV. General Conditions of Contract

1. Scope of Contract

This Contract shall include all such items, although not specifically mentioned, that can be reasonably inferred as being required for its completion as if such items were expressly mentioned herein. All the provisions of RA No. 9184 and its 2016 revised IRR, including the Generic Procurement Manual, and associated issuances, constitute the primary source for the terms and conditions of the Contract, and thus, applicable in contract implementation. Herein clauses shall serve as the secondary source for the terms and conditions of the Contract.

This is without prejudice to Sections 74.1 and 74.2 of the 2016 revised IRR of RA No. 9184 allowing the GPPB to amend the IRR, which shall be applied to all procurement activities, the advertisement, posting, or invitation of which were issued after the effectivity of the said amendment.

2. Sectional Completion of Works

If sectional completion is specified in the **Special Conditions of Contract** (SCC), references in the Conditions of Contract to the Works, the Completion Date, and the Intended Completion Date shall apply to any Section of the Works (other than references to the Completion Date and Intended Completion Date for the whole of the Works).

3. Possession of Site

- 4.1. The Procuring Entity shall give possession of all or parts of the Site to the Contractor based on the schedule of delivery indicated in the SCC, which corresponds to the execution of the Works. If the Contractor suffers delay or incurs cost from failure on the part of the Procuring Entity to give possession in accordance with the terms of this clause, the Procuring Entity's Representative shall give the Contractor a Contract Time Extension and certify such sum as fair to cover the cost incurred, which sum shall be paid by Procuring Entity.
- 4.2. If possession of a portion is not given by the above date, the Procuring Entity will be deemed to have delayed the start of the relevant activities. The resulting adjustments in contract time to address such delay may be addressed through contract extension provided under Annex "E" of the 2016 revised IRR of RA No. 9184.

4. The Contractor's Obligations

The Contractor shall employ the key personnel named in the Schedule of Key Personnel indicating their designation, in accordance with **ITB** Clause 10.3 and specified in the **BDS**, to carry out the supervision of the Works.

The Procuring Entity will approve any proposed replacement of key personnel only if their relevant qualifications and abilities are equal to or better than those of the personnel listed in the Schedule.

5. Performance Security

- 5.1. Within ten (10) calendar days from receipt of the Notice of Award from the Procuring Entity but in no case later than the signing of the contract by both parties, the successful Bidder shall furnish the performance security in any of the forms prescribed in Section 39 of the 2016 revised IRR.
- 5.2. The Contractor, by entering into the Contract with the Procuring Entity, acknowledges the right of the Procuring Entity to institute action pursuant to RA No. 3688 against any subcontractor be they an individual, firm, partnership, corporation, or association supplying the Contractor with labor, materials and/or equipment for the performance of this Contract.

6. Site Investigation Reports

The Contractor, in preparing the Bid, shall rely on any Site Investigation Reports referred to in the SCC supplemented by any information obtained by the Contractor.

7. Warranty

- 7.1. In case the Contractor fails to undertake the repair works under Section 62.2.2 of the 2016 revised IRR, the Procuring Entity shall forfeit its performance security, subject its property(ies) to attachment or garnishment proceedings, and perpetually disqualify it from participating in any public bidding. All payables of the GOP in his favor shall be offset to recover the costs.
- 7.2. The warranty against Structural Defects/Failures, except that occasioned-on force majeure, shall cover the period from the date of issuance of the Certificate of Final Acceptance by the Procuring Entity. Specific duration of the warranty is found in the **SCC**.

8. Liability of the Contractor

Subject to additional provisions, if any, set forth in the **SCC**, the Contractor's liability under this Contract shall be as provided by the laws of the Republic of the Philippines.

If the Contractor is a joint venture, all partners to the joint venture shall be jointly and severally liable to the Procuring Entity.

9. Termination for Other Causes

Contract termination shall be initiated in case it is determined *prima facie* by the Procuring Entity that the Contractor has engaged, before, or during the implementation of the contract, in unlawful deeds and behaviors relative to contract acquisition and implementation, such as, but not limited to corrupt, fraudulent, collusive, coercive, and obstructive practices as stated in **ITB** Clause 4.

10. Dayworks

Subject to the guidelines on Variation Order in Annex "E" of the 2016 revised IRR of RA No. 9184, and if applicable as indicated in the SCC, the Dayworks rates in the Contractor's Bid shall be used for small additional amounts of work only when the Procuring Entity's Representative has given written instructions in advance for additional work to be paid for in that way.

11. Program of Work

- 11.1. The Contractor shall submit to the Procuring Entity's Representative for approval the said Program of Work showing the general methods, arrangements, order, and timing for all the activities in the Works. The submissions of the Program of Work are indicated in the **SCC**.
- 11.2. The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work at intervals no longer than the period stated in the SCC. If the Contractor does not submit an updated Program of Work within this period, the Procuring Entity's Representative may withhold the amount stated in the SCC from the next payment certificate and continue to withhold this amount until the next payment after the date on which the overdue Program of Work has been submitted.

12. Instructions, Inspections and Audits

The Contractor shall permit the GOP or the Procuring Entity to inspect the Contractor's accounts and records relating to the performance of the Contractor and to have them audited by auditors of the GOP or the Procuring Entity, as may be required.

13. Advance Payment

The Procuring Entity shall, upon a written request of the Contractor which shall be submitted as a Contract document, make an advance payment to the Contractor in an amount not exceeding fifteen percent (15%) of the total contract price, to be made in lump sum, or at the most two installments according to a schedule specified in the SCC, subject to the requirements in Annex "E" of the 2016 revised IRR of RA No. 9184.

14. Progress Payments

The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. Except as otherwise stipulated in the SCC, materials and equipment delivered on the site but not completely put in place shall not be included for payment.

15. Operating and Maintenance Manuals

- 15.1. If required, the Contractor will provide "as built" Drawings and/or operating and maintenance manuals as specified in the **SCC.**
- 15.2. If the Contractor does not provide the Drawings and/or manuals by the dates stated above, or they do not receive the Procuring Entity's Representative's approval, the Procuring Entity's Representative may withhold the amount stated in the **SCC** from payments due to the Contractor.

Section V. Special Conditions of Contract

Special Conditions of Contract

The Intended Completion Date is sixty (60) calendar days which will commence within three calendar days from receipt of the Notice to Proceed. 4.1 three days from the receipt of the Notice to proceed 6 The site investigation reports are: Affidavit of Site Inspection 7.2 [In case of semi-permanent structures, such as buildings of types 1, 2, and 3 as classified under the National Building Code of the Philippines, concrete/asphalt roads, concrete river control, drainage, irrigation lined canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. 10 No dayworks are applicable to the contract. 11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	GCC Clause	
4.1 three days from the receipt of the Notice to proceed 6 The site investigation reports are: Affidavit of Site Inspection 7.2 [In case of semi-permanent structures, such as buildings of types 1, 2, and 3 as classified under the National Building Code of the Philippines, concrete/asphalt roads, concrete river control, drainage, irrigation lined canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. 10 No dayworks are applicable to the contract. 11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	2	<u> </u>
The site investigation reports are: Affidavit of Site Inspection [In case of semi-permanent structures, such as buildings of types 1, 2, and 3 as classified under the National Building Code of the Philippines, concrete/asphalt roads, concrete river control, drainage, irrigation lined canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. No dayworks are applicable to the contract. The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. The amount of the advance payment is 15% of the total contract price. The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
The site investigation reports are: Affidavit of Site Inspection [In case of semi-permanent structures, such as buildings of types 1, 2, and 3 as classified under the National Building Code of the Philippines, concrete/asphalt roads, concrete river control, drainage, irrigation lined canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. No dayworks are applicable to the contract. The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. The amount of the advance payment is 15% of the total contract price. The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
[In case of semi-permanent structures, such as buildings of types 1, 2, and 3 as classified under the National Building Code of the Philippines, concrete/asphalt roads, concrete river control, drainage, irrigation lined canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. 10 No dayworks are applicable to the contract. 11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	4.1	three days from the receipt of the Notice to proceed
[In case of semi-permanent structures, such as buildings of types 1, 2, and 3 as classified under the National Building Code of the Philippines, concrete/asphalt roads, concrete river control, drainage, irrigation lined canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. 10 No dayworks are applicable to the contract. 11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	6	The site investigation reports are: Affidavit of Site Inspection
and 3 as classified under the National Building Code of the Philippines, concrete/asphalt roads, concrete river control, drainage, irrigation lined canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. 10 No dayworks are applicable to the contract. 11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	7.2	
concrete/asphalt roads, concrete river control, drainage, irrigation lined canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. 10 No dayworks are applicable to the contract. 11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
canals, river landing, deep wells, rock causeway, pedestrian overpass, and other similar semi-permanent structures:] Five (5) years. 10 No dayworks are applicable to the contract. 11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
 and other similar semi-permanent structures:] Five (5) years. No dayworks are applicable to the contract. The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. The amount of the advance payment is 15% of the total contract price. The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE 		
10 No dayworks are applicable to the contract. 11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
11.1 The Contractor shall submit the Program of Work to the Procuring Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	1.0	
Entity's Representative for approval within ten (10) days of delivery of the Notice of award. 11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
the Notice of award. The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. The amount of the advance payment is 15% of the total contract price. The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	11.1	
11.2 The Contractor shall submit to the Procuring Entity's Representative for approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
approval an updated Program of Work every week, the Procuring Entity may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. 13 The amount of the advance payment is 15% of the total contract price. 14 The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
may withhold the amount of Five thousand pesos only if the contractor failed to Submit the updated program. The amount of the advance payment is 15% of the total contract price. The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	11.2	
failed to Submit the updated program. The amount of the advance payment is 15% of the total contract price. The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
The amount of the advance payment is 15% of the total contract price. The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
The Contractor may submit a request for payment for Work accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	12	1 1 9
accomplished. Such requests for payment shall be verified and certified by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
by the Procuring Entity's Representative/Project Engineer. 15.1 The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	14	
The date by which operating and maintenance manuals are required is NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE		
NOT LATER THAN 2 WEEKS AFTER THE COMPLETION OF THE	15 1	
	13.1	
PROTECT		PROJECT
The date by which "as built" drawings are required is <i>NOT LATER</i>		
THAN 2 WEEKS AFTER THE COMPLETION OF THE PROJECT		· · · · · · · · · · · · · · · · · · ·
The Procuring Entity may withhold the amount of PHP 52,081.67 of the	15.2	
remaining balance of the Contractor failed to submit or produce "as		
built" drawings.		1

Section VI. Specifications

	Seas No.		c of the Ph				50	IG LACON
			PALITY O		`E		(F)	
	INDIV	IDUAL :	 PROGR <i>i</i>	AM OI	WOF	RKS	1687	SA LAHA
NAME/L	OCATION OF PROJECT			Net A	rea		m3	50.25
				***************************************	Length		m	134 m.
СО	NCRETE OVERLAY AONG C.S. UM	ALI STE	REET	Width	Longin		m	2.50 m
CSI	JMALI STREET, BARANGAY -4, QU	INAI F	PAFTF					
0.0.	LAGUNA.	,,	. ,,	Thick	nes		m	0.15 m.
			1	CALE	NDAR [DAYS TO COMP	LETE	60 days
	CT CATEGORY :			DESI	RABLE:	STARTING DAT	E	
PROJEC	CT DESCRIPTION							
	CONCRETE OV	ERLAY A	ONG C.S	. UMAL	ISTRE	ET		
	MINIMUM EQUIPMENT REQUIREMENT			TEC	CHNICA	L PERSONNEL	REQUIR	RED
	Description	١	No.	D	escriptic	on		No.
					Forer			1
	CONCRETE MIXER	1				on / Carpenter		3
					Labore	r		6
		0007.6			MODI	,		
	ESTIMATED	%OF	F PROP	OSED.	WORK		CT COS	т
ltem No.	DESCRIPTION	TOTAL	UNIT	QTY.		TOTAL	1	UNIT COST
	MOBILIZATION / DEMOBILIZATION		l.s.	1				
II III	TEMPORARY FACILITIES CONCRETING		l.s.	1				
IV.	RSB		l.s.	1				
V.	FORMWORKS		l.s.	1				
VI.	PROJECT SIGNAGE		l.s.	1				
	SAFETY & HEALTH		l.s.	1				
VII.								
VII.		n º/-				0.00		0.00
VII.		0%	Direct	Cost		0.00)	0.00
VII.		0%	Direct Material			0.00		
VII.		0%	Direct Material	Cost		0.00	Php	0.00
VII.	Sub-Total	0%	Material	Cost		0.00	Php	0.00
VII.	Sub-Total	0%	Material	Cost	Php	0.00	Php Php	0.00
VII.	Sub-Total	0%	Material Labor	Cost Cost	Php		Php Php	0.00 0.00 0.00
VII.	Sub-Total	0%	Material Labor (Cost Cost Cost			Php Php	0.00 0.00 0.00
VII.		0%	Indirect OCM (5% Contractor VAT (5%	Cost Cost Cost Cost Profit Cost			Php Php Php	0.00 0.00 -
VIII.	Sub-Total Sub-Total	0%	Material Labor (Indirect OCM (5% Contractor	Cost Cost Cost Cost Profit Cost			Php Php Php	0.00 0.00 0.00

	Designation	No. of Person	No. of Day's	Daily Rate	Amount
١.	Labor				
	Construction Foreman	1	2		
	Mason / Carpenter	3	2		
	Laborer	6	2		
	Sub-Total for A				
	Name and Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
3.	Equipment				
	Sub - Total for B				
c.	Total (A+B)				
_					
	Name and Specification	Unit	Quantity	Unit Cost	Amount
D.	Materials				
	Sub-Total for D				
E	Direct Unit Cost (C+D)				
F	Overhead, Contingencies & Miscel	Ianeous (OCM)		of E	
G.	Contractor's Profit (CP)			of E	
н.	Value Added Tax (VAT)		5% of (E		
_	Total Unit Cost		(E + F +		

II.	TEMPORARY FACILI	TIES				
	Designation		No. of Person	No. of Day's	Daily Rate	Amount
١.	Labor					
	Construction Foreman		1	2		
	Mason / Carpente	r	2	2		
	Laborer		5	2		
	Sub-Total for A					
	Name and Capacity		No. of Units	No. of Hours	Hourly Rate	Amount
В.	Equipment					
	Sub - Total for B					
<u>C.</u>	Total (A+B)					
	Name and Sp	ecification	Unit	Quantity	Unit Cost	Amount
D.	Materials					
	30 - 2"X 3" X 12' Coco lumber		Bd.Ft	120		
	20 - 2"X 2" X 12' Coco lumber		Bd.Ft	80		
	1/4"X 4'X8' Ord. Plywood		Pcs.	10		
	Corrugated G.I. Sheet #10'		Pcs.	10		
	G.I. Tie Wire #16		Kgs.	8		
	Common Nail #1		Kgs.	2		
	Common Nail #2 Common Nail #3		Kgs.	3		
			Kgs.	4		
	Common Nail #4		Kgs.	5		
	Sub-Total for D					
Ε	Direct Unit Cost (C+D)					
F	Overhead, Contingencies & Miscellaneous (OCN			5% of E		
G.	Contractor's Profit (CP)			8%		
Н.	Value Added Tax (VAT)			5% of (E + F + G)		
	Total Unit Cost			(E + F +	G+H)	

Ш	CONCRETE AND MASONRY				
	Designation	No. of Person	No. of Day's	Daily Rate	Amount
	Labor				
	Construction Foreman	1	18		
	Mason-Carpenter-Steelman	3	18		
	Laborer	6	18		
	Sub-Total for A				-
	Name and Capacity	No. of Units	No. of Days	Daily Rate	Amount
	Equipment				
	Concrete Mixer	1	25		
	Sub - Total for B				-
c.	Total (A+B)				
	Name and Specification	Unit	Quantity	Unit Cost	Amount
D.	Materials				
	Portland Cement	Bags	302		
	Sand	cu.m.	25		
	Gravel	cu.m.	50		
_					
	Sub-Total for D				-
	Direct Unit Cost (C+D)	50/ 55		-	
	Overhead, Contingencies & Misco	ellaneous (OCM)	5% of E		
	Contractor's Profit (CP)		8% of E		-
•	Value Added Tax (VAT) Total Unit Cost		5% of (E + F + G) (E + F + G + H)		
	LIOTAL UNIT COST		(E+F+	υ+H)	-

IV.	RSB					
	Designation		No. of Person	No. of Day's	Daily Rate	Amount
A.	Labor				,	
	Construction Foreman		1	3		
	Steelman		1	3		
	Laborer		2	3		
	Sub-Total for A					<u>-</u>
	Name and	Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
В.	Equipment					- -
C.	Sub - Total for B Total (A+B)					<u>-</u>
С.	Total (A+b)					<u> </u>
	Name and Specification		Unit	Quantity	Unit Cost	Amount
D.	Materials					
	16mm Ø x 6.0m RSB		Pcs.	30.00		
	G.A. 16 G.I. Tie W	ire	kgs	10.00		
						-
	Sub-Total for D					-
E.	Direct Unit Cost (C+D)				-
F.	Overhead, Contingencies & Miscellaneous (OCM)		eous (OCM)	5% of E		-
G.			, ,	8% of E		-
Н.				5% of (E + F + G)		-
	Total Unit Cost			(E+F+G+H)		-


٧.	FORMWORKS				
	Designation	No. of Person	No. of Day's	Daily Rate	Amount
١.	Labor			July Hate	7 0 0
	A. Formworks				
	Construction Foreman	1	3		
	Carpenter	3	3		
	Laborer	3	3		
	В.				
	Sub-Total for A				-
	Name and Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
В.	Equipment				
	Sub - Total for B				-
c.	Total (A+B)				-
	Name and Specification	Unit	Quantity	Unit Cost	Amount
D.	Materials				
	A. FORMWORKS				
	40-2"X 3"X 12' (Coco Lumber)	bd. Ft	240		
	20-2"X 2"X 12' (Good Lumber)	bd. Ft	80		
	Common Nail # 2	kg.	8		
	Common Nail #3	kg.	8		
	Common Nail # 4	kg.	8		
	Sub-Total for D				-
Ε.	Direct Unit Cost (C+D)				-
=.	Overhead, Contingencies & Misc	ellaneous (OCM)	5%	of E	-
G.	Contractor's Profit (CP)	· , ,		of E	-
١.	Value Added Tax (VAT)			E + F + G)	-
	Total Unit Cost		(E+F+		


VI.	PROJECT SIGNAGE				
_	Designation	No. of Person	No. of Day's	Daily Rate	Amount
١.	Labor		•	-	
	Sub-Total for A				
	Name and Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
3.	Equipment Equipment	140. 01 011163	140. 01 110013	Hourry Rate	Amount
·-	Equipment				
	Sub - Total for B				-
<u>. </u>	Total (A+B)				-
	Name and Specification	Unit	Quantity	Unit Cost	Amount
).	Materials				
	SIGNAGE	LOT	1		
	SIGNAGE	LOT			
_					
	Sub-Total for D				-
	Direct Unit Cost (C+D)				-
	Overhead, Contingencies & Misce	llaneous (OCM)		of E	-
<u>. </u>	Contractor's Profit (CP)			of E	-
ì.				0\	
	Value Added Tax (VAT) Total Unit Cost		5% of (E	: + F + G) · G + H)	-

VII.	SAFETY AND HEALTH					
	Designation		No. of Person	No. of Day's	Daily Rate	Amount
Α.	Labor		1101011011		Daily Hade	
	Part time Safety Practit	oner	1	30		
	First Aider		1	30		
	Sub-Total for A					-
	Name and Capac	ty	No. of Units	No. of Day's	Daily Rate	Amount
В.	Equipment					
	Sub - Total for B					-
C.	Total (A+B)					-
	Name and Specifica	ition	Unit	Quantity	Unit Cost	Amount
D.	Materials					
	Safety Shoes		Man-Day	480		
	Safety Helmet		Man-Day	480		
	Safety Gloves		Man-Day	480		
	Body Harness		Man-Day	480		
	Sub-Total for D					
_	Direct Unit Cost (C+D)					-
E.	Overhead, Contingencies 8	Missollana	ous (OCM)	F0/	of E	<u>-</u>
F. G.	Contractor's Profit (CP)	iviisceiiane	ous (OCIVI)	8%		-
ы. Н.	Value Added Tax (VAT)			5% of (E		-
п.	Total Unit Cost			(E+F+		<u> </u>
i	TOTAL OTHE COST			(ETF+	G FII)	-

Section VII. Drawings

[Insert here a list of Drawings. The actual Drawings, including site plans, should be attached to this section, or annexed in a separate folder.]

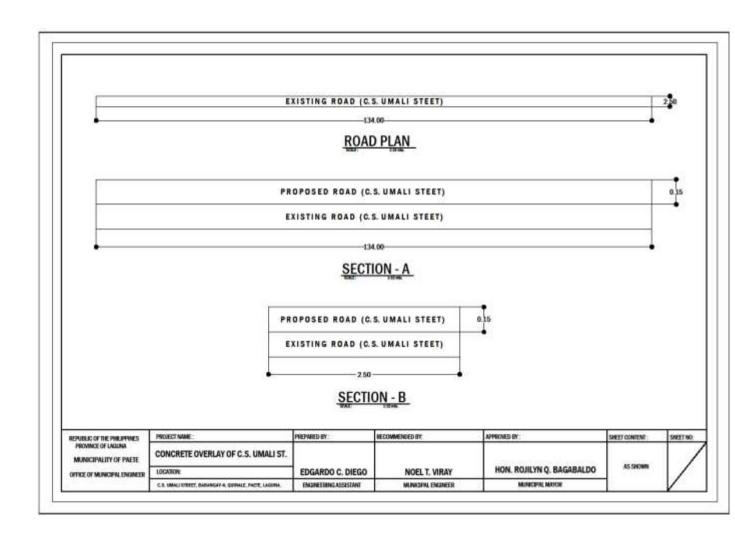

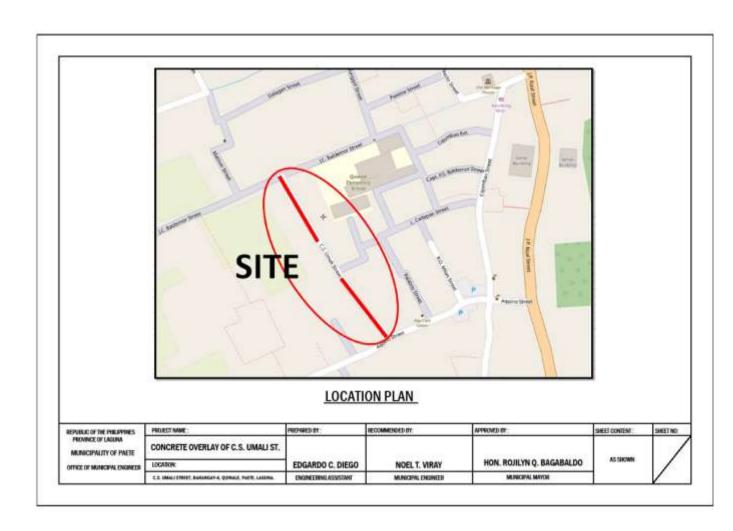


Section VIII. Bill of Quantities

Signature Box

A signature box shall be added at the bottom of each page of the Bill of Quantities where the authorized representative of the Bidder shall affix his signature. Failure of the authorized representative to sign each and every page of the Bill of Quantities shall be a cause for rejection of his bid.



Republic of the Philippines Province of Laguna





INDIVIDUAL PROGRAM OF WORKS

,						
NAME/LOCATION OF PROJECT			Net Ar	ea	m3	50.25
CONCRETE OVERLAY AONG C.S. UN	IALIQTE	DEET	Total L	-ength	m	134 m.
CONCRETE OVEREAT ACROSS. ON	IALISII	\LL1	Width		m	2.50 m
C.S. UMALI STREET, BARANGAY -4, QU	INIALE	DAETE	***************************************			
LAGUNA.	IIVALL, I	racic,	Thickne	es	m	0.15 m.
			CALEN	NDAR DAYS TO	COMPLETE	60 days
PROJECT CATEGORY :			DESIR	ABLE STARTIN	NG DATE	

PROJECT DESCRIPTION

CONCRETE OVERLAY AONG C.S. UMALI STREET

MINIMUM EQUIPMENT REQUIREMENT		TECHNICAL PERSONNEL REQUIRED		
Description	No.	Description	No.	
		Foreman	1	
CONCRETE MIXER	1	Mason / Carpenter	3	
		Laborer	6	

ESTIMATED COST OF PROPOSED WORK

14 a ma Na	DESCRIPTION	%OF		OTV		DIRECT COST		
Item No.	DESCRIPTION	TOTAL	UNIT	QTY.		TOTAL		UNIT COST
I	MOBILIZATION / DEMOBILIZATION		l.s.	1				
ll l	TEMPORARY FACILITIES		l.s.	1				
III	CONCRETING		l.s.	1				
IV.	RSB		l.s.	1				
V	FORMWORKS		l.s.	1				
VI.	PROJECT SIGNAGE		l.s.	1				
VII.	SAFETY & HEALTH		l.s.	1				
		0%				0.00		0.00
			Direct (Cost				
			Material	Cost			Php	0.00
			Labor (Cost			Php	0.00
	Sub-Total						Php	0.00
			Indirect	Cost	Php	0.00		
			OCM (5%)			Php	0.00
			Contractor		(8%)		Php	0.00
			VAT (5%)			Php	-
	Sub-Total		TOT	٩L			Php	0.00
	An	proved	Budget fo	or Con	tract		Php	0.00

	Designation	No. of Person	No. of Day's	Daily Rate	Amount
١.	Labor				
	Construction Foreman	1	2		
	Mason / Carpenter	3	2		
	Laborer	6	2		
	Sub-Total for A				
	Name and Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
3.	Equipment				
	Sub - Total for B				
С.	Total (A+B)				
	Name and Specification	Unit	Quantity	Unit Cost	Amount
D.	Materials				
	Sub-Total for D				
Ξ.	Direct Unit Cost (C+D)				
	Overhead, Contingencies & Misc	ellaneous (OCM)	% (of E	
3.	Contractor's Profit (CP)			of E	
1 .	Value Added Tax (VAT)			+ F + G)	
	Total Unit Cost		/	G+H)	

II.	TEMPORARY FACIL	ITIES				
	Design	nation	No. of Person	No. of Day's	Daily Rate	Amount
Α.	Labor					
	Construction For	eman	1	2		
	Mason / Carpent	er	2	2		
	Laborer		5	2		
	Sub-Total for A					-
	Name and	l Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
B.	Equipment					
C.	Sub - Total for B Total (A+B)					
-	Name and S	nocification	Unit	Quantity	Unit Cost	Amount
D.	Materials	pecification	Unit	Quantity	Unit Cost	Amount
υ.	iviateriais					
	30 - 2"X 3" X 12' (Coco lumbor	Bd.Ft	120		
	20 - 2"X 2" X 12' (Bd.Ft	80		
	1/4"X 4'X8' Ord.		Pcs.	10		
	Corrugated G.I. S		Pcs.	10		
	G.I. Tie Wire #16		Kgs.	8		
	Common Nail #1		Kgs.	2		
	Common Nail #2		Kgs.	3		
	Common Nail #3		Kgs.	4		
	Common Nail #4		Kgs.	5		
						-
						-
						<u>-</u>
	Sub-Total for D					<u>-</u>
Ε.	Direct Unit Cost (C+I	0)				
<u>F.</u>	Overhead, Continge		neous (OCM)	5%	of E	
<u></u> G.	Contractor's Profit ((00:00)		of E	-
Н.	Value Added Tax (V/			5% of (E		-
	Total Unit Cost			(E + F +	•	-
				, ,		

Ш	CONCRETE AND MASONRY				
	Designation	No. of Person	No. of Day's	Daily Rate	Amount
١.	Labor		•	,	
	Construction Foreman	1	18		
	Mason-Carpenter-Steelman	3	18		
	Laborer	6	18		
	Sub-Total for A				-
	Name and Capacity	No. of Units	No. of Days	Daily Rate	Amount
3.	Equipment				
	Concrete Mixer	1	25		
	Sub - Total for B				-
<u>. </u>	Total (A+B)				<u>-</u>
	Name and Specification	Unit	Quantity	Unit Cost	Amount
).	Materials				
	Portland Cement	Bags	302		
	Sand	cu.m.	25		
	Gravel	cu.m.	50		
	Sub-Total for D				
	Direct Unit Cost (C+D)				-
	Overhead, Contingencies & Misce	llaneous (OCM)		of E	-
ì.	Contractor's Profit (CP)			of E	-
l	Value Added Tax (VAT)			: + F + G)	
	Total Unit Cost		(E + F +	G+H)	-

IV.	RSB				
	Designation	No. of Person	No. of Day's	Daily Rate	Amount
Α.	Labor				
	Construction Foreman	1	3		
	Steelman	1	3		
	Laborer	2	3		
	Sub-Total for A				
	Name and Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
В.	Equipment	11010101111		, , , , , , , , , , , , , , , , , , , ,	
					-
					-
	Sub - Total for B				-
C.	Total (A+B)				-
	Name and Specification	Unit	Quantity	Unit Cost	Amount
D.	Materials		Quarterty	0	7 iiii Guine
	16mm Ø x 6.0m RSB	Pcs.	30.00		
	G.A. 16 G.I. Tie Wire	kgs	10.00		
					-
	Sub-Total for D				
E.	Direct Unit Cost (C+D)				
<u>F.</u>	Overhead, Contingencies & Misce	ellaneous (OCM)	5%	of E	-
G.	Contractor's Profit (CP)			of E	-
Н.	Value Added Tax (VAT)		5% of (E	:+F+G)	-

٧.	FORMWORKS				
	Designation	No. of Person	No. of Day's	Daily Rate	Amount
١.	Labor			July Hate	7 0 0
	A. Formworks				
	Construction Foreman	1	3		
	Carpenter	3	3		
	Laborer	3	3		
	В.				
	Sub-Total for A				-
	Name and Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
В.	Equipment				
	Sub - Total for B				-
c.	Total (A+B)				-
	Name and Specification	Unit	Quantity	Unit Cost	Amount
D.	Materials				
	A. FORMWORKS				
	40-2"X 3"X 12' (Coco Lumber)	bd. Ft	240		
	20-2"X 2"X 12' (Good Lumber)	bd. Ft	80		
	Common Nail # 2	kg.	8		
	Common Nail #3	kg.	8		
	Common Nail # 4	kg.	8		
	Sub-Total for D				-
Ε.	Direct Unit Cost (C+D)				-
=.	Overhead, Contingencies & Misc	ellaneous (OCM)	5%	of E	-
G.	Contractor's Profit (CP)	· , ,		of E	-
١.	Value Added Tax (VAT)			E + F + G)	-
	Total Unit Cost		(E+F+		

VI.	PROJECT SIGNAGE				
_	Designation	No. of Person	No. of Day's	Daily Rate	Amount
١.	Labor		•	-	
	Sub-Total for A				
	Name and Capacity	No. of Units	No. of Hours	Hourly Rate	Amount
3.	Equipment Equipment	140. 01 011163	140. 01 110013	Hourry Rate	Amount
·-	Equipment				
	Sub - Total for B				-
<u>. </u>	Total (A+B)				-
	Name and Specification	Unit	Quantity	Unit Cost	Amount
).	Materials				
	SIGNAGE	LOT	1		
	SIGNAGE	LOT			
_					
	Sub-Total for D				-
	Direct Unit Cost (C+D)				-
	Overhead, Contingencies & Misce	llaneous (OCM)		of E	-
<u>. </u>	Contractor's Profit (CP)			of E	-
ì.				0\	
	Value Added Tax (VAT) Total Unit Cost		5% of (E	: + F + G) · G + H)	-

VII.	SAFETY AND HEALTH							
	Designation		No. of Person	No. of Day's	Daily Rate	Amount		
Α.	Labor		1101011010		Daily Hade			
	Part time Safety Practitioner		1	30				
	First Aider		1	30				
	Sub-Total for A					-		
	Name and Capaci	ty	No. of Units	No. of Day's	Daily Rate	Amount		
B.	Equipment							
	Sub - Total for B		ļ			-		
C.	Total (A+B)					-		
	Name and Specification		Unit	Quantity	Unit Cost	Amount		
D.	Materials		Oilit	Quantity	Offit Cost	Amount		
υ.	Safety Shoes		Man-Day	480				
	Safety Helmet		Man-Day	480				
	Safety Gloves		Man-Day	480				
	Body Harness		Man-Day	480				
	Sub-Total for D					-		
E.	Direct Unit Cost (C+D)					-		
F.	Overhead, Contingencies & Miscellaneou		ous (OCM)	5% of E		-		
G.	Contractor's Profit (CP)		8%	of E				
Н.	Value Added Tax (VAT)			5% of (E + F + G)		-		
	Total Unit Cost			(E + F +	G+H)	-		

Section IX. Checklist of Technical and Financial Documents

Notes on the Checklist of Technical and Financial Documents

The prescribed documents in the checklist are mandatory to be submitted in the Bid, but shall be subject to the following:

- a. GPPB Resolution No. 09-2020 on the efficient procurement measures during a State of Calamity or other similar issuances that shall allow the use of alternate documents in lieu of the mandated requirements; or
- b. any subsequent GPPB issuances adjusting the documentary requirements after the effectivity of the adoption of the PBDs.

The BAC shall be checking the submitted documents of each Bidder against this checklist to ascertain if they are all present, using a non-discretionary "pass/fail" criterion pursuant to Section 30 of the 2016 revised IRR of RA No. 9184.

Checklist of Technical and Financial Documents

I. TECHNICAL COMPONENT ENVELOPE

Class "A" Documents

Leg	al Do	ocuments
	(a)	Valid PhilGEPS Registration Certificate (Platinum Membership) (all pages);
	(b)	or Registration certificate from Securities and Exchange Commission (SEC), Department of Trade and Industry (DTI) for sole proprietorship, or Cooperative Development Authority (CDA) for cooperatives or its equivalent document; and
	(c)	Mayor's or Business permit issued by the city or municipality where the principal place of business of the prospective bidder is located, or the equivalent document for Exclusive Economic Zones or Areas; and
	(e)	Tax clearance per E.O. No. 398, s. 2005, as finally reviewed and approved by the Bureau of Internal Revenue (BIR).
<u>Tec</u>	chnica	d Documents
	(f)	Statement of the prospective bidder of all its ongoing government and private contracts, including contracts awarded but not yet started, if any, whether similar or not similar in nature and complexity to the contract to be bid; and
	(g)	Statement of the bidder's Single Largest Completed Contract (SLCC) similar to the contract to be bid, except under conditions provided under the rules; and
	(h)	Philippine Contractors Accreditation Board (PCAB) License;
	(i)	or Special PCAB License in case of Joint Ventures; and registration for the type and cost of the contract to be bid; and Original copy of Bid Security. If in the form of a Surety Bond, submit also a certification issued by the Insurance Commission;
	(j)	or Original copy of Notarized Bid Securing Declaration; and Project Requirements, which shall include the following:
		a. Organizational chart for the contract to be bid;
		b. List of contractor's key personnel (<i>e.g.</i> , Project Manager, Project Engineers, Materials Engineers, and Foremen), to be assigned to the contract to be bid, with their complete qualification and experience data;
		c. List of contractor's major equipment units, which are owned, leased, and/or under purchase agreements, supported by proof of ownership or certification of availability of equipment from the equipment lessor/vendor for the duration of the project, as the case may be; and
	(k)	Original duly signed Omnibus Sworn Statement (OSS);

<u>and</u> if applicable, Original Notarized Secretary's Certificate in case of a corporation, partnership, or cooperative; or Original Special Power of Attorney of all members of the joint venture giving full power and authority to its officer to sign the OSS and do acts to represent the Bidder.

	Fin	iancial	Documents				
		(1)	The prospective bidder's audited financial statements, showing, among				
			others, the prospective bidder's total and current assets and liabilities,				
			stamped "received" by the BIR or its duly accredited and authorized				
			institutions, for the preceding calendar year which should not be earlier than				
	_		two (2) years from the date of bid submission; and				
		(m)	The prospective bidder's computation of Net Financial Contracting Capacity (NFCC).				
	Class "B" Documents						
		(n)	If applicable, duly signed joint venture agreement (JVA) in accordance with				
			RA No. 4566 and its IRR in case the joint venture is already in existence;				
			<u>or</u>				
			duly notarized statements from all the potential joint venture partners stating				
			that they will enter into and abide by the provisions of the JVA in the				
			instance that the bid is successful.				
II.	FIN	ANCI	AL COMPONENT ENVELOPE				
		(o)	Original of duly signed and accomplished Financial Bid Form; and				
Other documentary requirements under RA No. 9184							
		(p)	Original of duly signed Bid Prices in the Bill of Quantities; and				
		(q)	Duly accomplished Detailed Estimates Form, including a summary shee				
		\ 1 /	indicating the unit prices of construction materials, labor rates, and equipmen				
			rentals used in coming up with the Bid; and				
		(r)	Cash Flow by Quarter.				

